


SCHEMATIC SKETCH

WORK PROGRESS STATUS

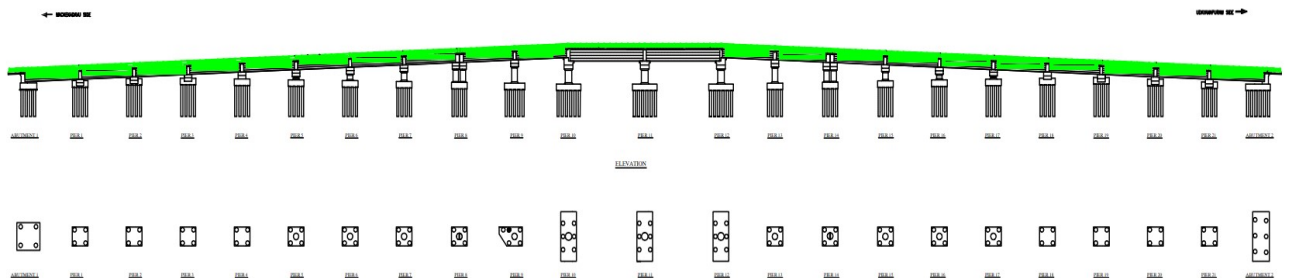

STRUCTURE	TOTAL No.	COMPLETED	BALANCE	REMARK
PILE (300mm)	101	97	4	4 pile not done (300mm x 300mm)
PILE CAP	23	21	2	2 pile not done (300mm x 300mm)
PIER	15	15	0	15 pile not done (300mm x 300mm)
PIER CAP	23	23	0	23 pile not done (300mm x 300mm)
GRADER	88	6	82	82 pile not done (300mm x 300mm)
DECK SLAB	22	0	22	22 pile not done (300mm x 300mm)
KEEL	22	0	22	22 pile not done (300mm x 300mm)
HANDRAIL	22	0	22	22 pile not done (300mm x 300mm)
BENCH	22	0	22	22 pile not done (300mm x 300mm)

 To be completed

PROJECT:-	CONSTRUCTION OF A BRIDGE AT MAKKEKADAVU, CONNECTING MAKKEKADAVU KAYALA AND UDAYANAPURAM IN ACROSS VEMBANAD KAYAL IN ALAPPUZHA DIST
CLIENT:-	PUBLIC WORK DEPARTMENT GOVERNMENT OF KERALA
CONTRACTOR:-	CHERIAN VARKEY CONSTRUCTION CO. Pvt LTD
